




SR-91/I-605/I-405 “Hot Spots” Program

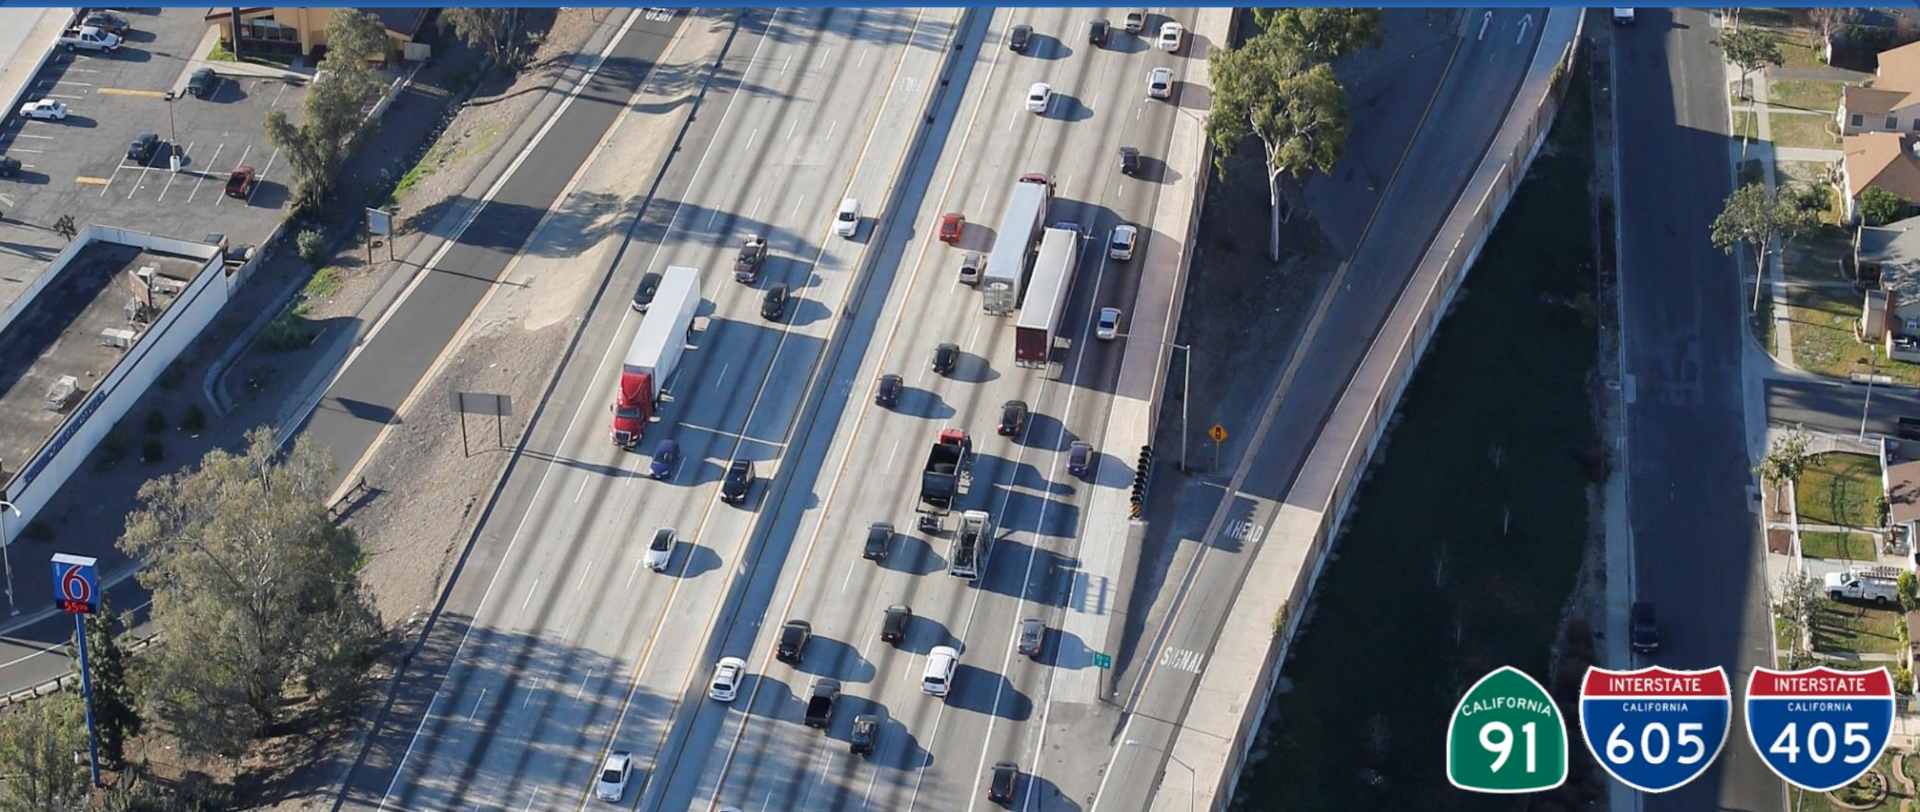

Metro

January 2022

Program Overview



I-605 / Valley Blvd.

SR-60 / 7th Ave.

I-605 / Beverly Blvd.

SR-91 / I-605

SR-91 / Central - Acacia

SR-91 / Atlantic - Cherry

I-605 / South St.

I-605 / I-10

I-605 / SR-60

I-605 / I-5


I-605 / I-105

\$10+ Billion

**30+ Arterial
Intersection
Improvements**



Metrolink

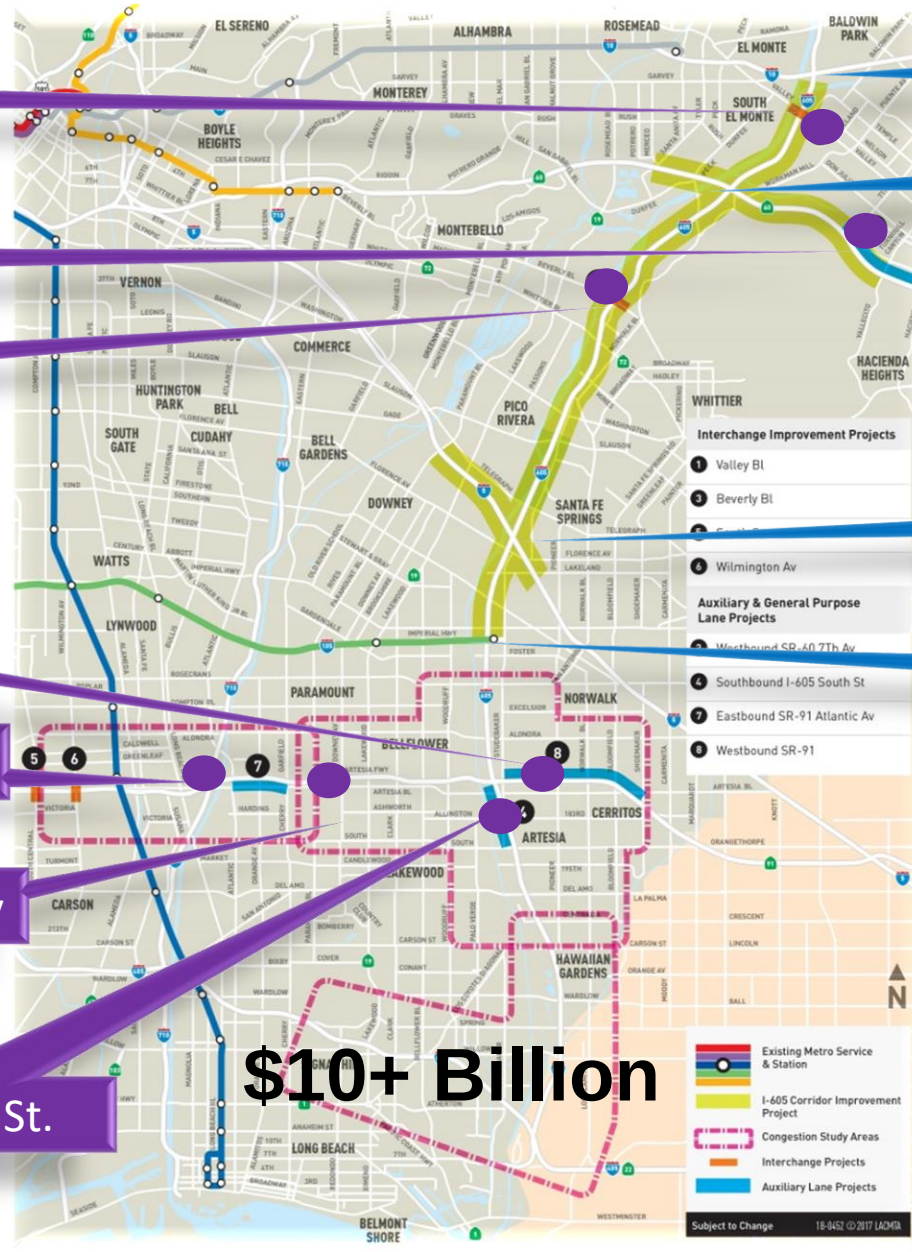

I-605 / South St. Interchange



Project Summary

- Improve weaving on SB I-605 by widening South St off-ramp
 - Add second right-turn lane (two left and two right-turns total)
 - Provides standard deceleration distance

Status Update

- Final Design Complete January 2020
- Advertisement January 2023
- Construction Start anticipated Fall 2023

Multimodal Elements

- Bicycle and pedestrian signage
- LED lighting in pedestrian/bicycle accessible areas



I-605 / SR-91 Interchange



Project Summary


- Westbound SR-91 widening to add a lane between Shoemaker and Alondra

Status Update

- Resolution of Pioneer off-ramp design – Oct 2021
- Total TCEP Funding awarded about \$70 million PS&E & Construction
- Final design completion anticipated Spring 2023

Multimodal Elements

- Class II bicycle lane will be striped on Pioneer Blvd
- Bicycle and pedestrian signage and LED lighting in pedestrian/bicycle accessible areas

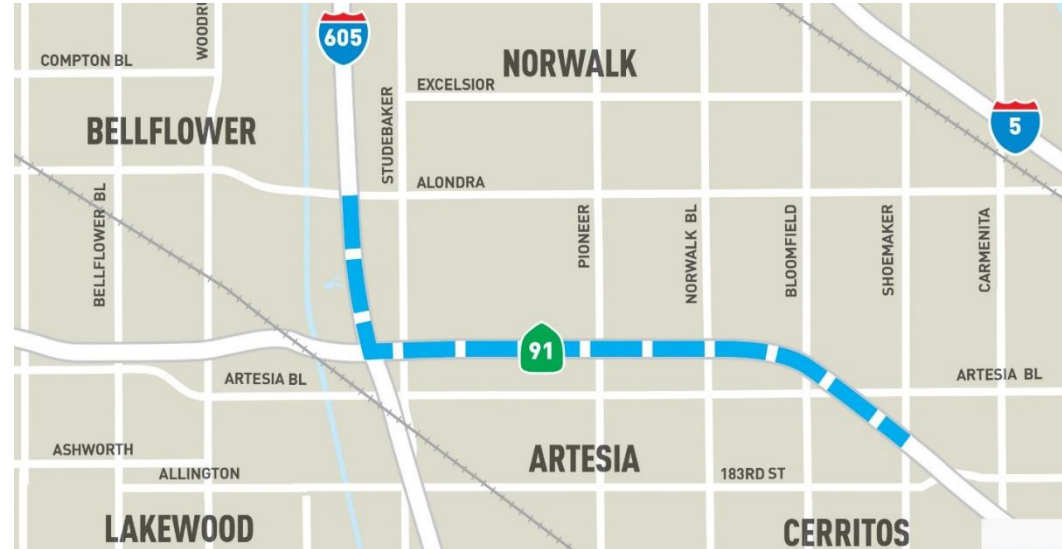

SR-91 / Central to Acacia



Project Summary


- Addresses weaving issue caused by the closely spaced on/off ramps
 - C-D Road in both directions
- Improvements on interchanges & mainline

Status Update

- PAED completion anticipated July 2021
- 95% PS&E completion anticipated June 2023
- RTL Sept 2025

Multimodal Elements

- Class II buffered lanes
- Bicycle and pedestrian signage and LED lighting

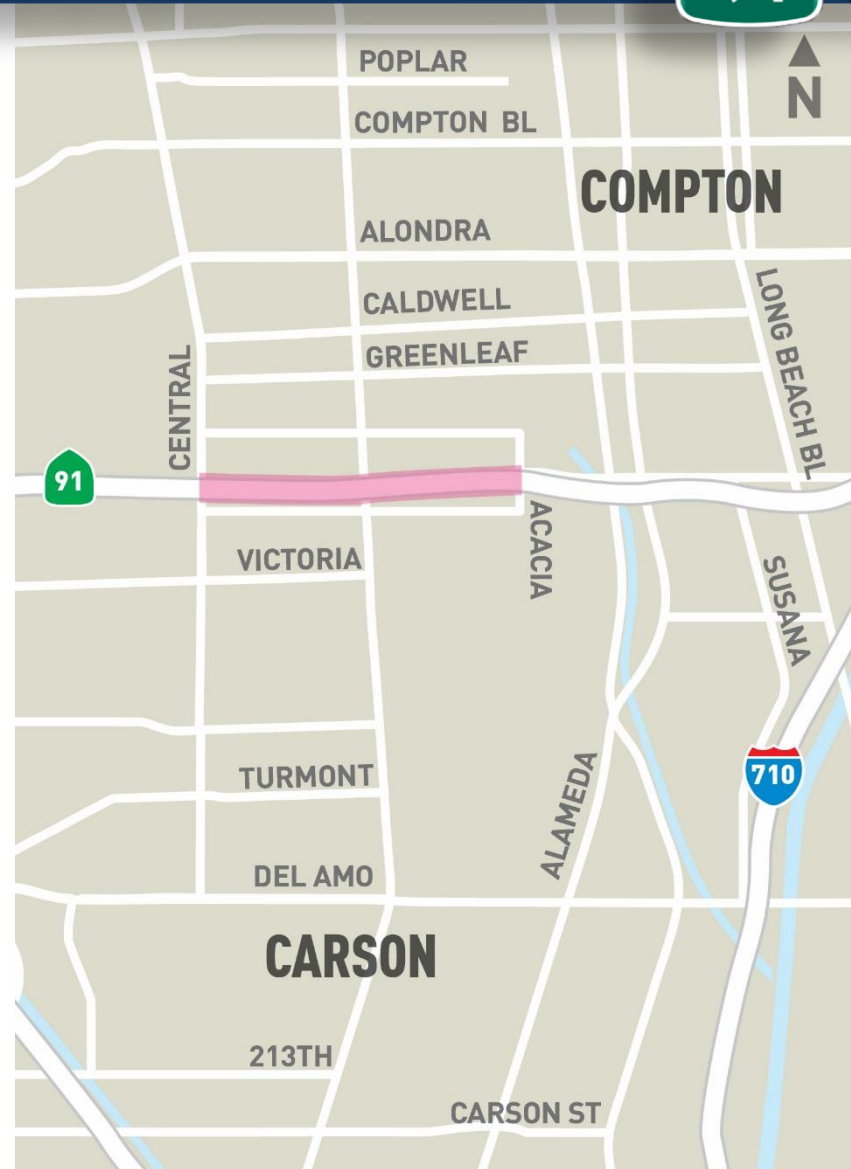

SR-91 / Atlantic to Cherry



Project Summary


- Address weaving issue on mainline
- Add EB SR-91 auxiliary lane from I-710 Connectors to Cherry Ave off-ramp

Status Update

- PAED completion May 2021
- PS&E completion May 2022
- Construction anticipated Early 2024
- Awarded TCEP (SB1) funding for Construction - \$ 48 Million

Multimodal Elements

- Retaining walls to facilitate implementation of Hamilton Loop Park Project
- Provision of upgraded landscaping and lighting within park areas

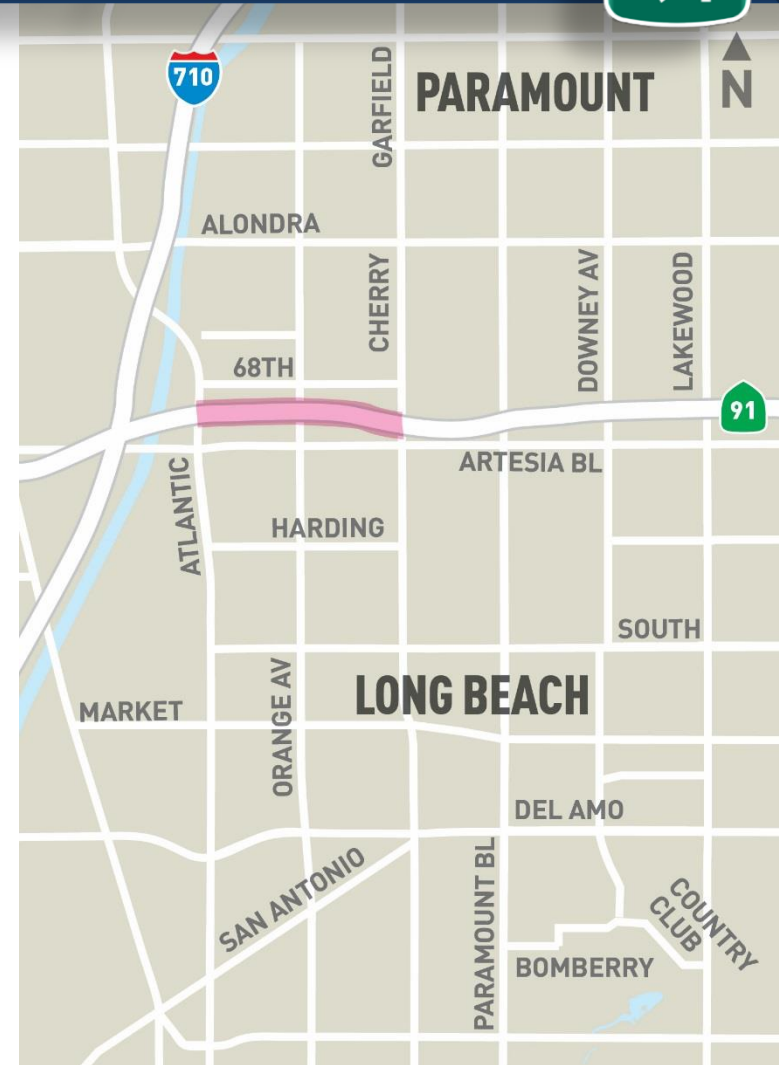

I-605 / Beverly Blvd. Interchange



Project Summary


- Eliminate short weaving length between existing loop ramps
 - Implement diamond interchange
- Provide all movements at intersection & signalize
- PAED & PS&E Contract Award 2018

Status Update

- PAED completed in March 2020
- Final Design completed in 2022. Caltrans Coop Agreement Pending
- Construction bid in 2024

Multimodal Elements

- Provision of high visibility crosswalk
- Accommodation for future Class II bicycle lane on overcrossing

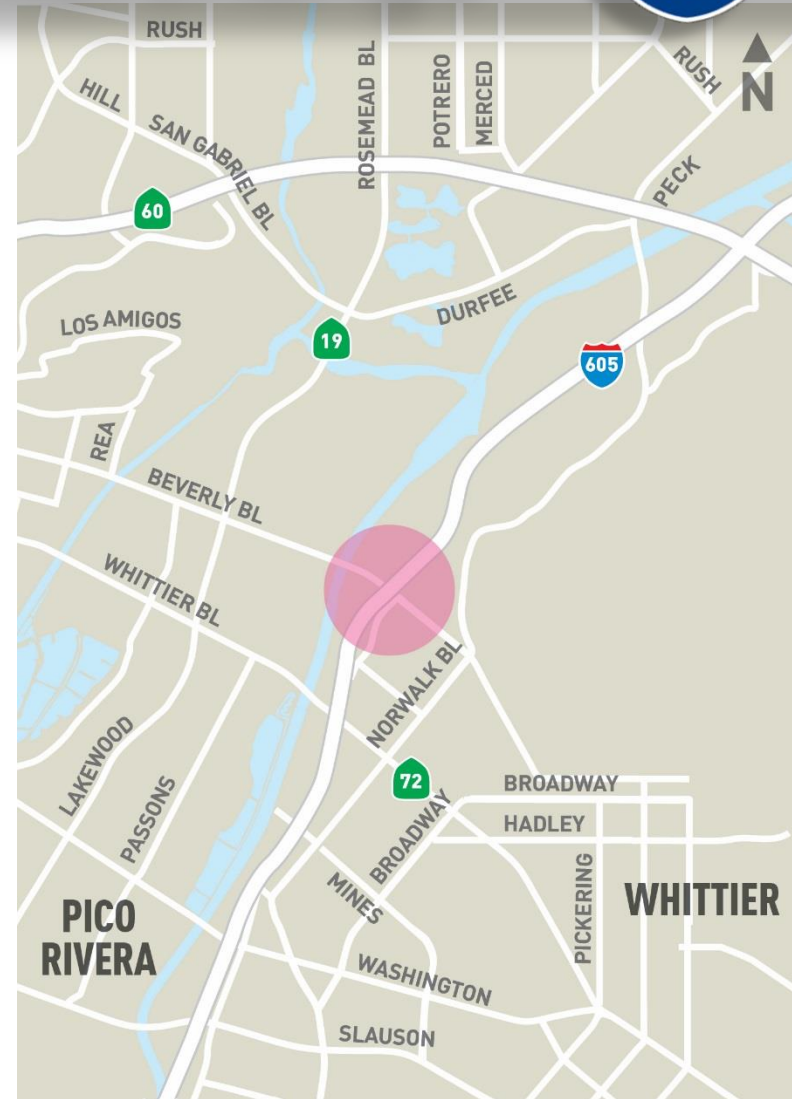

I-605 / Valley Blvd. Interchange



Project Summary

- Reconfigure freeway on and off ramps
- Increase ramp storage, reduce queueing
- Improve truck access/maneuverability
- Modify signals (traffic and railroad)
- Upgrade local streets (Valley & Temple)
- Provide railroad/roadway safety upgrades

Status Update

- PAED approval May 2021
- Final PS&E expected October 2023

Multimodal Elements

- Upgraded ADA infrastructure (curb ramps, sidewalks, driveways, signals)
- Bicycle and pedestrian signage, signals and LED lighting for pedestrian/bicycle accessible areas



SR-60 / 7th Ave. Interchange



Project Summary


- Add lane on WB off-ramp
- Addresses geometric, operational, and safety issues of the ramps/local street intersections
 - Queue spillback onto freeway

Status Update

- CE approved 8/5/20
- Design phase on hold pending funding for construction phase

Multimodal Elements

- Signage for bicycle and pedestrian
- LED lighting in pedestrian/bicycle accessible areas

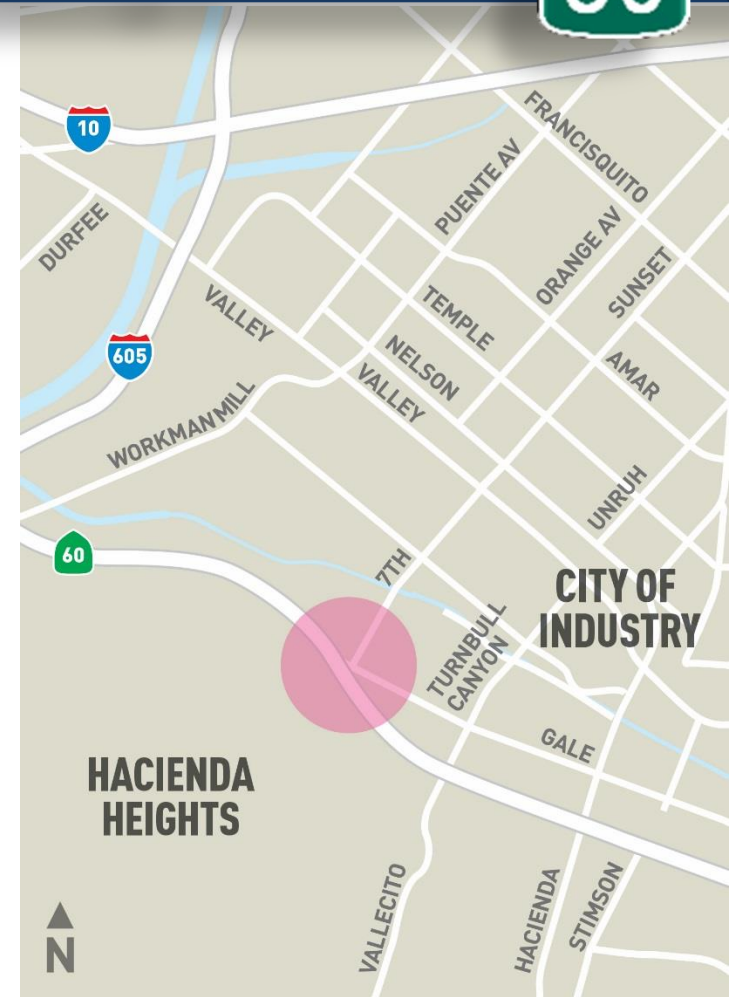

SR-72 / Whittier Blvd




Project Summary

- Address congestion at Santa Fe Springs Road and Painter Avenue
- Add additional through/turn lanes and reconstruct curb ramps, passageways, driveways, sidewalks to ADA standards

Status Update

- PAED completion 2018
- Design completion 2022
- ROW complete at Santa Fe Springs Road
- ROW underway at Painter Avenue
- Construction in 2023 & 2024

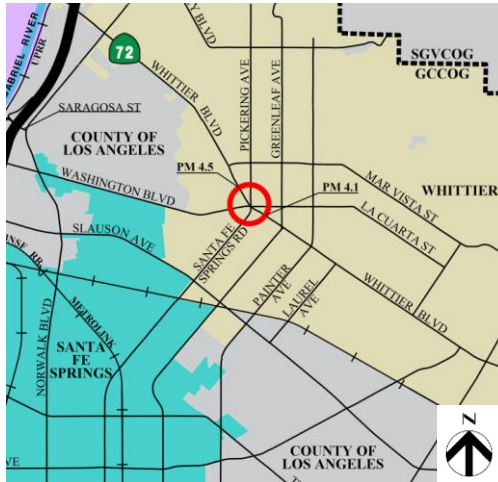

**Santa Fe
Springs Road**



**Painter
Avenue**



I-605 Program



Gateway Cities Complete Streets & Highways Programs

Ernesto Chaves
Executive Officer
chavese@metro.net

I-605 Valley Blvd & SR-60/7th Ave

Michelle Smith
Project Manager
SmithMi@metro.net

SR-72 Whittier

Julio Perucho
Project Manager
PeruchoJ@metro.net

SR-91 Cherry & I-605 Beverly

Lucy Delgadillo
Project Manager
delgadillolu@metro.net

<https://www.metro.net/projects/i-605-corridor-hot-spots-program/>

WB SR-91 & Arterial Programs

Carlos Montez
Project Manager
montezc@metro.net

<https://www.metro.net/projects/i-605-corridor-hot-spots-program/>
